


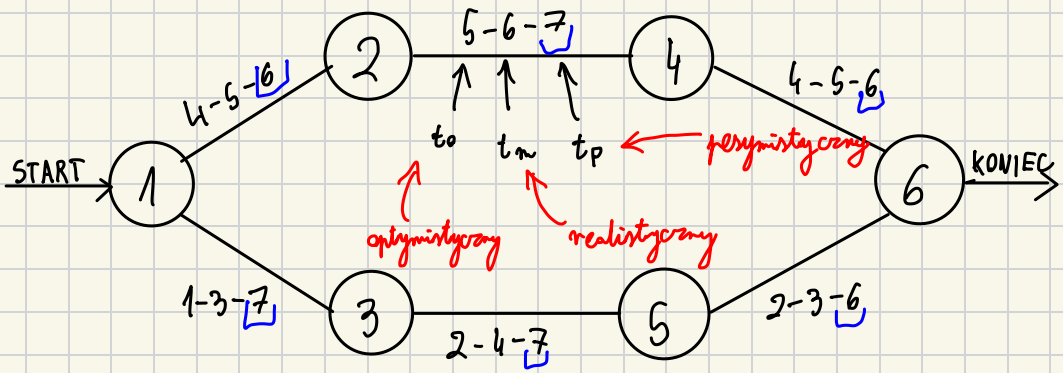

Zadanie	t_o	t_m	t_p	t_e	σ^2
1-2	4	5	6	5	0,11
1-3	1	3	7	3,33	1,80
2-4	5	6	7	6	0,11
3-5	2	4	7	4,17	0,69
4-6	4	5	6	5	0,11
5-6	2	3	6	3,33	0,44

$$t_e = \frac{t_o + 4t_m + t_p}{6}$$

$$\sigma^2 = \frac{(t_o - t_p)^2}{36}$$

$$|S_{1-2-4-6}| = 16 \leftarrow \text{ścieżka krytyczna}$$

$$|S_{1-3-5-6}| = 10,83$$

$$\sigma^2 = 0,33$$

$$2,13$$


POMIAR

METODA EVM

Po co?

Co?

Jak?

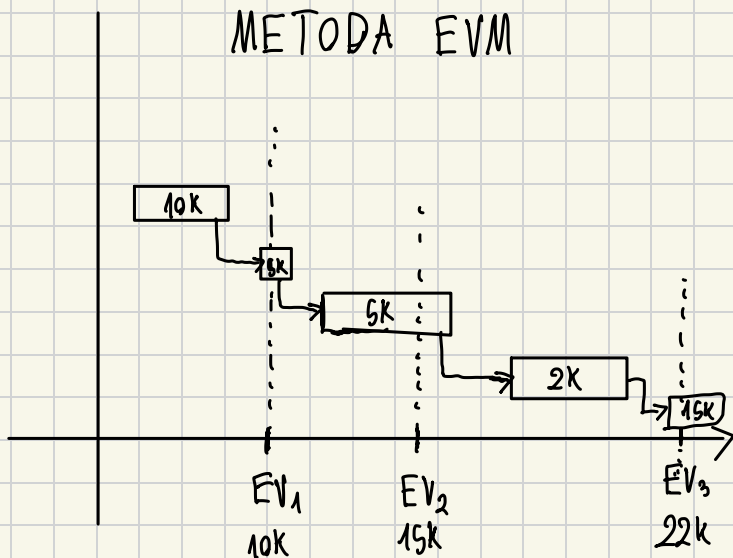

PV / BCWS - Planned Value / Budgeted Cost for Work Scheduled

BAC - Budget At Completion

EV / BCWP - Earned Value / Budget Cost for Work Performed

Koszt

$SV = EV - PV$ - Schedule Variance

AC / ACWP - Actual Cost / Actual Cost for Work Performed

$CV = EV - AC$ - Cost Variance

Wsp. sprawnosci

$CPI = \frac{EV}{AC}$ Cost Performance Index

$SPI = \frac{EV \cdot t}{PV}$ Schedule Performance Index

